

MODULE 2: PREPARING FOR SUPPLY CHAIN TRANSFORMATION





Module 2 Overview

Preparing for Supply Chain Transformation

- Section A: Select Supply Chain Transformation Drivers
- Section B: Assess Supply Chain Current State
- Section C: Conceptualize the Future-State Supply Chain Operating Model
- Section D: Identify Initiatives to Address Gaps
- Section E: Initiate Transformation Work Streams and Projects
- Section F: Develop and Iterate Preliminary Transformation Business Cases
- Section G: Perform Post-Approval Tasks





SECTION A: SELECT SUPPLY CHAIN TRANSFORMATION DRIVERS





Section A Overview

Section A Learning Objectives

- Create a portfolio or program charter to authorize and guide the transformation.
- Use tools such as STEEPLE or PESTLE to assess external transformation drivers.
- Assess current and needed technology.
- Conduct supply chain maturity assessments.
- Assess readiness for transformation.



Topic 1: Create Portfolio Charter and Select Supply Chain Transformation Tools

Create Portfolio Charter for Design Team and Core Steering Team

Charter content details:


Scope and Background and business need

Aligned assumptions and expectations

Formal contract of personnel involvement Selected metrics, schedule, deliverables, etc.




SCOR DS and DCM for Supply Networks

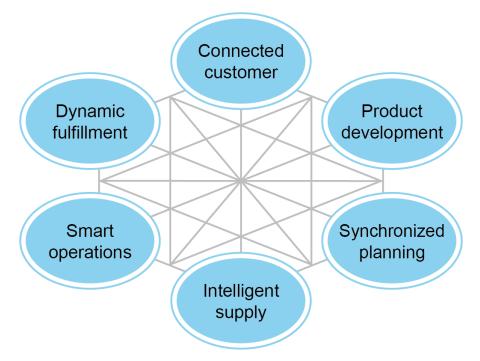

Adapted: Copyright ASCM. Used with permission.



Environmental Scanning

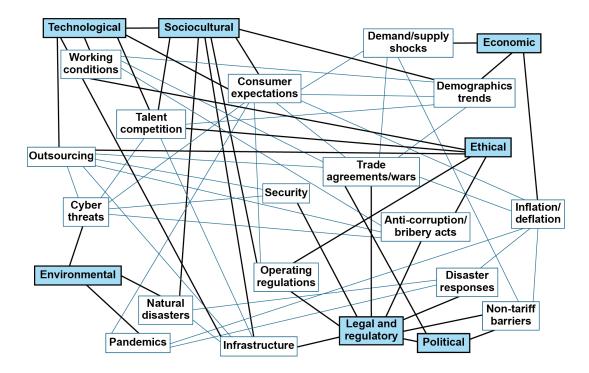

Macroeconomics and the Macro Environment

Traditional macroeconomic drivers include currency fluctuations and supply and/or demand shocks.

Currency fluctuations may occur as inflation or deflation or through changes in currency exchange rates.

Demand and supply shocks may be driven by multiple reasons.



Industry Characteristics

Product characteristics

Manufacturing and production processes

Lean versus resilient supply chains






Market Characteristics


10

- Supply chains must be set up and run to support the organization's strategy.
- Market characteristics may change due to many reasons:





STEEPLE and PESTLE/PESTEL

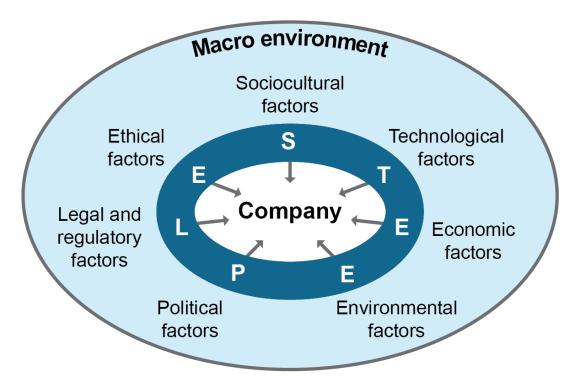



STEEPLE and PESTLE/PESTEL, continued

Factor	Details and Examples
Sociocultural	 Changing population demographics Economic inequality Consumer sustainability activism Pandemics
Technological	 Emerging and speculative technology Labor availability (remote work) Cyber threats
Economic	Macroeconomic conditionsConsumer confidence
Environmental	 Growing consumer interest in sustainable practices Natural events and trends along with reactions to those events and trends Environmental disasters



STEEPLE and PESTLE/PESTEL, continued

Factor	Details and Examples
Political	 Economy's political, governmental, or institutional environment Public policies Risk of sudden change (elections, civil unrest)
Legal/ regulatory	 Enacted laws and regulations International drivers National laws and regulations
Ethical	 Business ethics Good governance Social responsibility Moral standards Ethical sourcing Accountability and sustainability



Industry 4.0 and Supply Chain Transformation


Industry 4.0

 A concept of organizational and technological changes along with value chain integrations and new business models development that are driven by customer needs and mass customization requirements and enabled by innovation technologies, connectivity, and information technology integration. (*Dictionary*)





Supply Chain Transformation Technology Selection/ Utilization Process

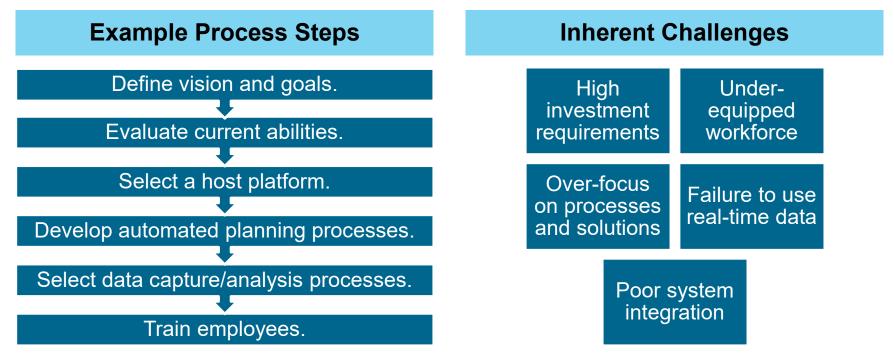



Sustainability and Social Responsibility Imperative


- Supply chain produces majority of pollution and greenhouse gas emissions.
- Climate change:
 - Particular concern for the growth and production of food
 - Results in supply chain disruptions around the world
 - Important to balance efforts with cost efficiency



Voice of the Customer Insights

Novel product uses	Quality needs and expectations	Interest in new products and services	
New business models	Speed, dependability, and cost objectives	Customer satisfaction	
Branding improvements	Customer loyalty issues	Competitor product information	



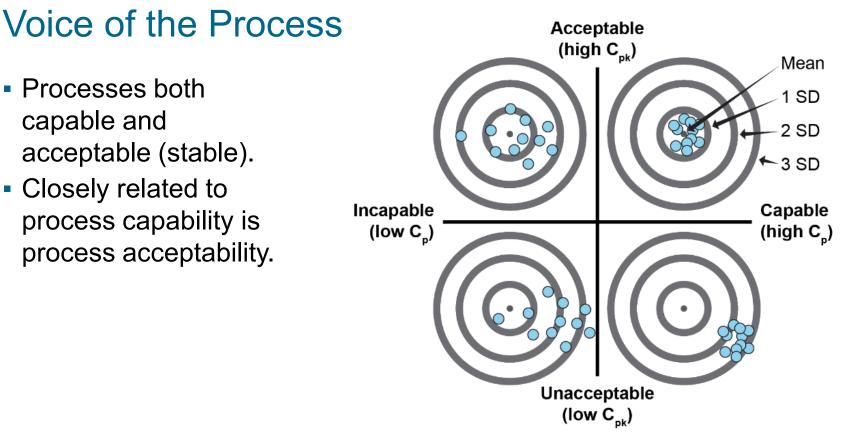



Measuring Process Capability and Acceptability

$$C_p = \frac{\text{USL} - \text{LSL}}{6 \times \text{SD}}$$

$$C_{pk}$$
 = Lesser of $\frac{(USL - Mean)}{3 \times SD}$ or $\frac{(Mean - LSL)}{3 \times SD}$



Voice of the Business and Voice of the Employee

Voice of the Business


- Captures stakeholder needs and requirements
- May include
 - Shareholders/owners
 - Leadership
 - Boards of directors

Voice of the Employee

- Captures requirements of individual employees
- May include opinions on
 - Culture
 - Policies
 - Systems
 - Infrastructure
 - Working conditions
 - Transformation strategy



Balancing Preferences from the Voices





Requirements for Success in Digital Transformation

Defined vision

Clear goals

Defined success metrics (should include both traditionally important metrics and metrics dealing with supply chain complexity)



Data Management and Data Analytics Technologies

- As digitalization of the supply chain is implemented, massive amounts of data will be generated.
- Gaps between current and desired technology capabilities may be related to multiple dimensions.





Data Technology

Big Data	ΙΟΤ	SCADA	Sensors and Telematics
 Volume Variety Velocity Value Veracity 	 Manufacturing processes Goods/materials movement Environmental conditions Equipment status Unexpected deviations Product utilization 	 Monitoring and control focus Legacy SCADA systems are increasingly able to integrate with other systems. 	 Provide process visibility and automation Include photosensors, RFID, lasers, lidar




Data Technology, continued

DSS	AI	Cloud Computing	Blockchain
 Assists in selecting and evaluating courses of action Draws from other systems (ERP, APS, etc.) 	 Useful areas: Forecasting and sourcing improvement Operations optimization Automation Decision support Targeted marketing/pricing 	 Data storage accessible over internet Benefits include increased collaboration, hardware costs shifted, scalable, flexible 	 Reliable, secure method of tracking goods movements Benefits include reliable evidence, automated capture and distribution of data, preventing counterfeits





Product Life Cycle Management

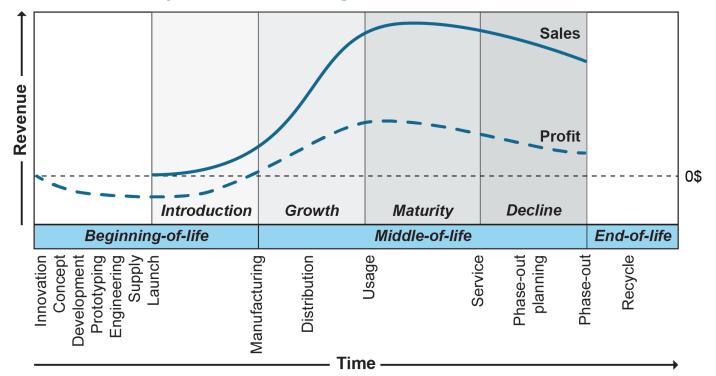



Enterprise Resource Planning

Transactionally focused


Modular options

Central database for master data

Designed for interoperability with other systems



Advanced Planning and Scheduling

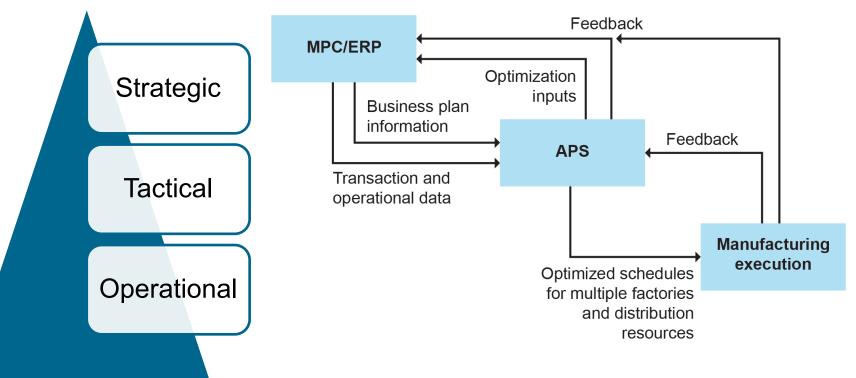



Warehouse Management Systems

Database Inclusions

- Product profiles
- Slot locations
- Labor standards for planning
- Shipper information
- Customer information

WMS Functions

- Manage orders and inventory.
- Organize warehouse work.
- Monitor and analyze performance.



CMMS and RDSM

CMMS

- Software programs that monitor assets
- Can reduce unexpected breakdowns
- Can optimize life span of equipment

RDSM

Provides

- Plant-level coordination at supply network level
- Real-time visibility into supply disruptions and unmet demand



Digital Supply Chain Control Towers

- Allow customers to act on the information they provide
- Dependent on
 - IOT
 - RFID
 - Sensors
 - Telematics
 - ERP
 - Warehouse management
 - Transportation management



Supply Chain Event Management

- Simulates, controls, and responds to unplanned events and exceptions to planned events
- Reduces or eliminates customer service errors
- Active visibility, enabling the following activities for events
 - Monitoring
 - Measurement
 - Notification
 - Simulation
 - Control



Topic 6: Maturity Assessments


Maturity Assessment Tools

- Identify multiple levels or categories of organizational performance
- Multiple models:
 - PwC model accompanying SCORmark
 - Deloitte-TM Forum model
 - Area-specific models (GHSC, Demand-Driven Institute's Adaptive Enterprise Model Development Path)
 - Gartner model



Topic 6: Maturity Assessments

Digital Capabilities Model (DCM) for Supply Networks



Topic 6: Maturity Assessments

Capability Maturity Model Integration

Capabilities

- Capability Level 0: Incomplete
- Capability Level 1: Performed
- Capability Level 2: Managed
- Capability Level 3: Defined

Maturity Levels

- Maturity Level 1: Initial
- Maturity Level 2: Managed
- Maturity Level 3: Defined
- Maturity Level 4: Quantitatively managed
- Maturity Level 5: Optimizing



Topic 7: Identify Common Misalignments


Common Misalignment Causes

Unspoken disagreement	Ineffective organizational structure
Vague goals	Poor interoperability
Failure to achieve ROI	M&A side effects
Lack of organizational support	Poor processes
Fragmented strategies	Improper supply chain scope change
Poorly executed S&OP	Poor plan for scalability
Lack of plan for technology investment	Failure to identify improvement areas
Mismatched structure/culture and ERP	Change management failure



Topic 7: Identify Common Misalignments


Assess Readiness for Transformation





Topic 7: Identify Common Misalignments

Common Forms of Bias







SECTION B: ASSESS SUPPLY CHAIN CURRENT STATE





Section B Overview

Section B Learning Objectives

- Define a balanced set of integrated metrics.
- Convert generic metrics to organization-specific versions.
- Plan and conduct data gathering.
- Prioritize supply chain design through segmentation.
- Perform geographic and process mapping.
- Benchmark process and performance metrics.
- Create detailed as-is maps, models, and diagrams.
- Understand how to use the staple-yourself-to-an-order walkthrough/interview process.
- Analyze defects and identify performance gaps.



Topic 1: Define To-Be Metrics and Use Them to Analyze As-Is Performance

Define a Balanced Set of Integrated Metrics

Several methods can be used to select a balanced set of integrated metrics:

Use metrics from established framework, like SCOR DS.

Fill out benchmarking survey, e.g., SCORmark, and select from results.

Use set of metrics from internal or consulting source.

Supplement one of these sources with custom metrics.



Convert Generic Metrics to Organization-Specific Versions

Examine/Discuss

- Metric's standard definition
- Calculation
- Data collection process

Define

- Exact point at which each process or calculation starts
- Exact point at which each process or calculation ends

Organize

- All metrics descriptions should be recorded in one file.
- Data collected and calculated should also be gathered in one location.





Prioritize Supply Chain Design Using Supply Chain Segmentation

Supply Chain			Customers								
Segmen	tation		West	Coast			East	Coast			
Products		S-Mart	Auto Bros	Costking	Carfix	Vehlicle Proof	Night Drive	The Mall	Automotive Ecommerce		
Automotive	Private	Х	Х	Х					Х		
Oil	Branded	Х		Х	Х	Х	Х	Х	X		
Cleaning	Private	Х	Х	Х					X		
Products	Branded	Х			Х		Х				
Lubricants	Private		Х	Х		Х		Х			
LUDICAILS	Branded	Х		Х	Х			Х	Х		




Prioritize Supply Chain Design Using Supply Chain Segmentation, continued

Supply Chain Customer					S				
Segmen	tation	West Coast East Coast							
Produ	icts	S-Mart	Auto Bros	Costking	Carfix	Vehlicle Proof	Night Drive	The Mall	Automative Ecommerce
Automotive	Private	4,535,345	5,676,576	12,313,543	-	-	-	-	64,758
Oil	Branded	543,545	-	65,464	2,345,765	464,767	876,868	4,564	343,454
Cleaning	Private	43,543	675,757	3,424,234	-	-	-	-	544,657
Products	Branded	86,787	-	-	3,454,354	-	543,534	-	-
Lubricants	Private	-	9,756,345	67,657	-	56,455	-	34,344	-
Lubricants	Branded	1,325,568	-	8,678,557	12,347	-	-	34,456	45,356
	Total	6,534,788	16,108,678	24,549,455	5,812,466	521,222	1,420,402	73,364	998,225
Annual	Revenue				53,005,387	3,013,213			



Topic 2: Prioritize the Supply Chain to be Designed, Set Attribute Targets, Map, and Benchmark

Set Superior, Advantage, or Parity Targets for Major Attributes

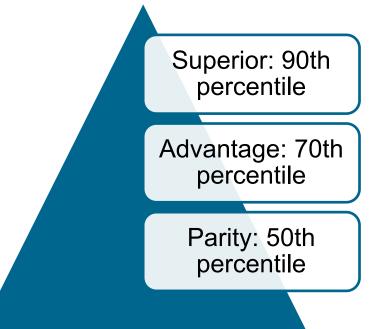

Building a Competitive Strategy Matrix for Multiple Channels and Markets

Attribute	West Coast Distributor	East Coast Distributor	West Coast Bulk Chemicals	West Coast Bulk Oils/Lubricants
Reliability	Advantage	Parity	Advantage	Advantage
Responsiveness	Parity	Advantage	Parity	Parity
Agility	Parity	Parity	Parity	Parity
Cost	Advantage	Advantage	Superior	Superior
Profit	Parity	Parity	Parity	Parity
Assets	Superior	Superior	Advantage	Advantage
Environmental	Parity	Parity	Advantage	Advantage
Social	Advantage	Advantage	Parity	Parity




Topic 2: Prioritize the Supply Chain to be Designed, Set Attribute Targets, Map, and Benchmark

Perform Geographic and Process Mapping of Selected Chain

Issues that may be identified


- Too many nodes or too few
- Nodes not in optimal location
- Too many or too few processes
- Incorrect processes or incorrect process placement
- Too many or too few links or suboptimal links

As-Is Geographic Mapping

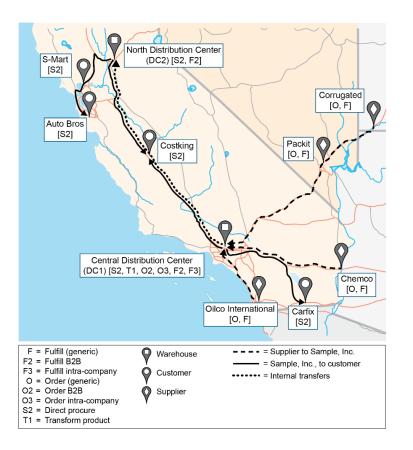



As-Is Process Mapping (Thread Diagram)

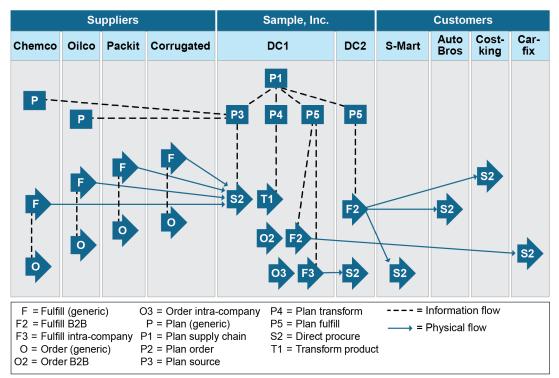



Benchmarking Principles

General Principles

- Benchmarking relies on use of standardized metrics.
- Can be linked to clear lines of responsibility.
- Avoids overly subjective metrics.

Industry Comparison Benchmarking

- Industry comparison benchmarking can be done without submitting any data to a third party.
- Organizations can get access to industry comparison benchmarking data from many sources.



Third-Party Scorecard Survey Benchmarking (e.g., SCORmark)


Attribute	Metrics	Target Performance	Your Organization	Parity (50%)	Advantage (70%)	Superior (90%)	Gap to Target
Reliability	Perfect customer order fulfillment	Advantage	70%	X 77%	85%	93%	-15%
Responsiveness	Customer order fulfillment cycle time	Parity	6	9.1	7 🗙	4	3.1
Agility	Supply chain agility, strategic (days)	Parity	35	X 30	25	20	-5
Cost	Total supply chain management cost (% of revenue)	Advantage	8%	8.70% <mark>X</mark>	5%	2.40%	-3%
Profitability	EBIT (as a % of revenue)	Parity	16%	14%	X 17%	20%	2%
Assets	Cash-to-cash cycle time (days)	Superior	52	55.4 <mark>X</mark>	30.5	0	-52
Environmental	Waste generated (metric tons)	Parity	14.3	X 13.4	11.2	9.2	-0.9
Social	Training (hours per year)	Advantage	80	X 82.1	91.5	100.1	-11.5
						X Your org	ganization

Source: Adapted from SCOR-Professional Training. Used with permission. Values are for example only.




Third-Party Scorecard Survey Benchmarking (e.g., SCORmark), continued

Cash-to-Cash Cycle Time Your Score: 52 days You chose the superior target for this metric. While you have scored above parity by -3.4 days, your target gap is -52 days.



Metric	Actual	Parity 50th	Advantage 70th	Superior 90th	Gap
Cash-to-Cash Cycle Time (Days)	52	55.4	30.5	0	-52
Days Payables Outstanding	55	66	60	54	-1
Days Sales Outstanding	27	30	33	39	3
Inventory Days of Supply	80	90	60	15	-65
Finished Goods	67	50	30	10	-57
Work In Process	1	1	0.5	0	0
Raw Material	12	20	15	5	-7

= Targeted competitive level



Refining As-Is Geographic and Process Maps to Better Study Gaps

- Benchmarking results will reveal areas that require collection of additional as-is information.
- Refinements may include
 - Geographic and process maps
 - Detailed process models
 - RACI diagrams.



Gather Data Using Interviews to Make Detailed Process Models

Cover crosssection of organization.

Include supply chain partners.


Be both horizontal and vertical.

Avoid questionnaires.

Encourage open, honest discussion.



Detailed As-Is Process Models (Workflow Diagrams)

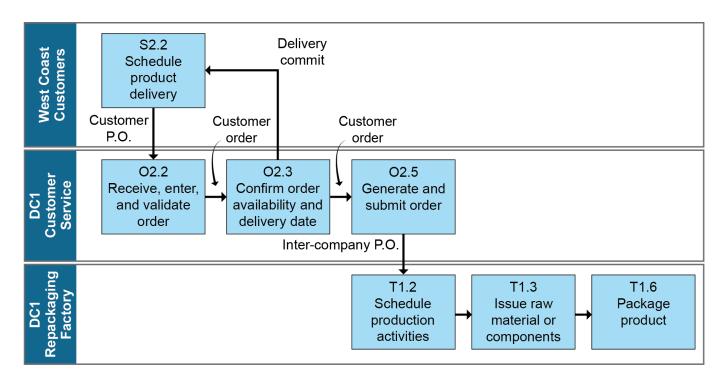




Create Detailed As-Is Process Models and RACI Diagrams (i.e., SCOR DS Level 4)

Review master data for processes. Pre-populate "staple yourself" template copies. Inform interviewees about transformation program at each new site. Conduct walkthrough and interview at each location in process.



RACI Diagrams for Process Flows

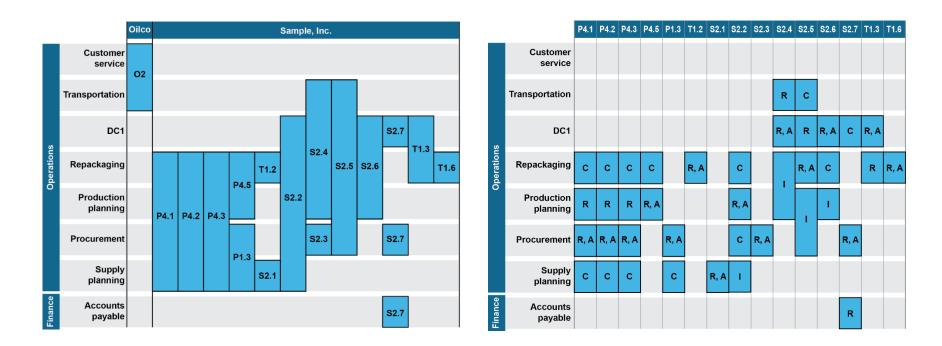



Gap Assessments, Defects, Supply Chain Standards/ Frameworks: Metric Defect Analysis Steps

Assemble actual metric data.

Define what constitutes a defect.

Segment the data to understand the problem.

Determine the defect rate for each defect type.

Prioritize the defects.



Analysis for Attribute Areas






Analysis for Perfect Customer Order Fulfillment

30.0%	20.0%	3.0%	3.0%	4.0%
Perfect Customer Order Fulfillment (RL.1.1) Failure Rate	Incomplete Shipments Rate (RL.2.1)	Missed Original Customer Commit Date Rate (RL.2.2)	Documentation Error Rate (RL.2.3)	Condition Error Rate (RL.2.4)
Wrong quantity assembled and shipped	0.25%			
Insufficient ordering due to actual demand > forecast	15.0%			
Late raw material pickup	0.25%			
Products mislabeled	0.25%			0.5%




Analysis for Customer Order Fulfillment Cycle Time

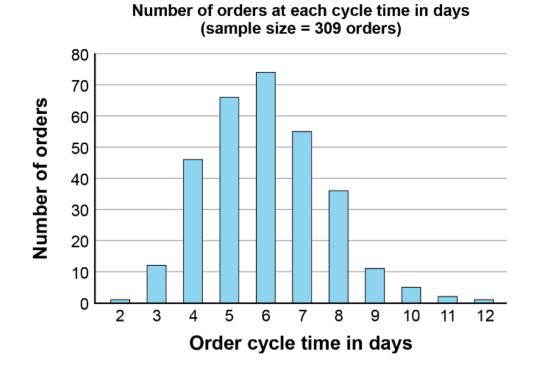



Analysis for Supply Chain Agility


Supply chain agility can be measured in SCOR DS as a strategic or an operational metric.

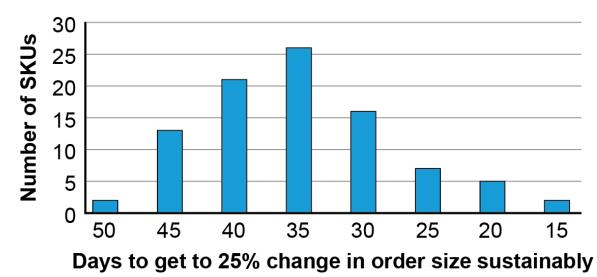



Analysis for Supply Chain Agility, continued

Each failure can then be given additional scrutiny.

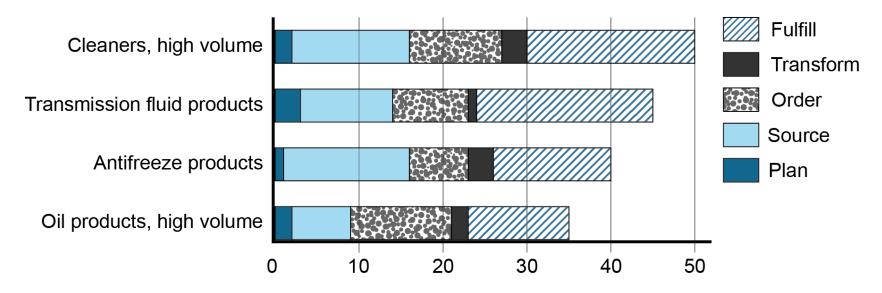




Analysis for Total Supply Chain Management Cost

Create a Pareto chart to

- Analyze total supply chain management cost
- Rank all costs from highest to lowest.

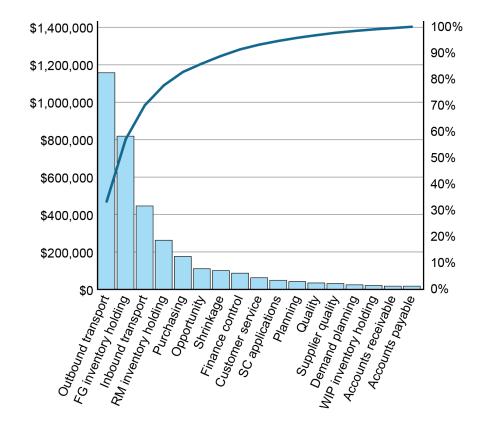




Analysis for Cash-to-Cash Cycle Time

Cash-to-Cash Cycle Time = Inventory Days of Supply + Days Sales Outstanding – Days Payables Outstanding

66

Cash-to-Cash Cycle Time Your Score: 52 days You chose the superior target for this metric. While you have scored above parity by -3.4 days, your target gap is -52 days.



Metric	Actual	Parity 50th	Advantage 70th	Superior 90th	Gap
Cash-to-Cash Cycle Time (Days)	52	55.4	30.5	0	-52
Days Payables Outstanding	55	66	60	54	-1
Days Sales Outstanding	27	30	33	39	3
Inventory Days of Supply	80	90	60	15	-65
Finished Goods	67	50	30	10	-57
Work In Process	1	1	0.5	0	0
Raw Material	12	20	15	5	-7

= Targeted competitive level





SECTION C: CONCEPTUALIZE THE FUTURE-STATE SUPPLY CHAIN OPERATING MODEL





Section C Overview

Section C Learning Objectives

- Prioritize defects by defect rate and problem weight.
- Convert approved scenarios into projects or work streams.
- Conduct an alternatives analysis.
- Develop supply chain models and simulations.
- Define and test to-be documentation and to-be geographic and process maps.
- Create a supply chain capability model.



Prioritize Defects by Defect Rate and Problem Weight

Final two steps of metric defect analysis:

- Prioritizing defects
- Estimating amount of work to get to root cause

Requires understanding consequence of problem

• Defect rate × problem weight = problem impact



Assemble Documentation on Defect Rates and Disconnects or Blockers (Abridged)

ID	SCOR DS Level 2 and Level 3 Defects	Defect Rate
1.0.0	Perfect customer order fulfillment failure rate (RL.1.1)	30.0%
1.1.0	Incomplete shipments rate (RL.2.1)	15.0%
1.1.1	No available-to-promise (ATP) inventory at ordering	5.0%
1.1.2	Inventory reallocated to priority customer	5.0%
1.1.3	Late raw material pickup	2.5%
1.1.4	Insufficient ordering due to actual demand > forecast	1.0%
1.1.5	Wrong products picked and shipped	0.5%
1.1.6	Wrong quantity picked and shipped	0.5%



Plan for a Brainstorming Session to Define Problems and Problem Impact

Determine the
right persons to
participate.Invite
participants
early.

Provide participants with an overview.

Select an appropriate venue.

Select a leader.





Conduct a Brainstorming Event to Define Problems and Problem Impact

Brainstorming Types

- Individual (homework)
- Group (event)

Brainstorming Event Activities

- Initial full-group brainstorming session (e.g., 1 hour)
- Small teams make specific area affinity diagrams (2 hours)
- Small teams define problem per affinity group (2 hours)
- Final full-group meeting to discuss results (1 hour)

Topic 1: Prioritize Defects, Identify Projects, and Analyze Alternatives

Convert Approved Scenarios into Projects or Work Streams

- Results of data collection, benchmarking, and brainstorming should be collected in project portfolio planning spreadsheet.
 - Sort and filter spreadsheet to group similar concepts
- Another brainstorming session can identify potential projects or work streams by grouping scenarios.

Topic 1: Prioritize Defects, Identify Projects, and Analyze Alternatives

Determine Analysis Criteria and Process

- Analysis criteria: how organization defines a winning alternative
 - Feasibility, budget, or strategic alignment checks
- Multiple tools can be used to develop alternatives.
 - Project alternatives generation brainstorming event
 - Further investigate problems (fifth why)
 - External consultants
 - Supply chain literature
 - Alternatives risk assessment
 - Modeling or simulation

Types of Alternatives

Design team develops set of alternative ways to solve organization's problem statements.

- Standardize
- Improve
- Add/eliminate
- Change a process
- Renegotiate



Automate part or most of process.

Alter operating rules or algorithms.

Alter business rules, policies, or procedures, such as new warranty policy.

Perform processes in different location or transfer to different party.

Change organizational structure and accountability for specific processes.



Topic 1: Prioritize Defects, Identify Projects, and Analyze Alternatives

Sample, Inc., Alternatives List

- Sample, Inc., design team's analysis:
 - A push supply chain driven by forecasting
 - Actual demand not shared
 - Historical supplier issues resulted in inventory buffers on consignment
- SCOR DS has standardized codes for practices (BP).
 - E.g., BP.156 Collaborative Planning, Forecasting, and Replenishment (CPFR)



Simulate/Model Supply Chain Value in Its To-Be State

- Prior to settling on a particular solution:
 - Test and validate potential projects for financial value, strategic fit, feasibility, and potential for gap reduction.
 - Develop a set of test scenarios.
 - Validate test scenarios based on analysis criteria.
- Scenarios that fail may be included on a wish list.

Perform Scenario Testing

Practice	Test(s) Conducted	Result	Rationale
BP.021 Sales and Operations Planning (S&OP)	High-level walkthrough of the scenario led by a team member with S&OP expertise	Fail	Add to wish list. We have few product families and products and low mix/volume variance, so S&OP would have limited ROI. S&OP is internally focused, but current inventory issues are related to customer forecasts and consignment stocks.
BP.034 Extend Inventory Planning Using Collaboration	High-level walkthrough of the scenario led by a team member with S&OP expertise	Fail	Add to wish list. This extends S&OP to customers and would address inventory but requires S&OP maturity.
BP.156 Collaborative Planning, Forecasting, and Replenishment	Walkthrough of scenario led by a consultant	Pass	CPFR addresses delayed or missing promotion and demand change data and plan buy-in.




Define and Test To-Be Documentation

Metric	Actual	Mandate	Change	To-Be Goal
Cash-to-cash cycle time	52 days	0 days	–53 days	–1 day
Days sales outstanding	27 days		0 days	27 days
Days payables outstanding	55 days		0 days	55 days
Inventory days of supply	80 days		–53 days	27 days
• Days, RM	12 days		–7 days	5 days
• Days, WIP	1 day		0 days	1 day
• Days, FG	67 days		<i>−50 + 4 = −46 days</i>	21 days



Create To-Be Geographic Maps, Process Maps, and RACI Diagrams

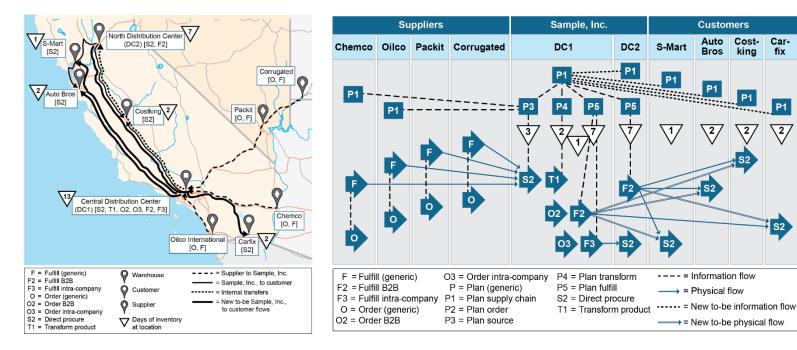

Car-

fix

P1

2

S2

Create a Supply Chain Capability Model

- Clearly align capabilities with organizational and supply chain strategy and ensure feasibility (check maturity).
- People skills (HS) from SCOR DS
 - E.g., HS.0032 Customer or Supplier Communication
- ASCM's Digital Capabilities Model (DCM) for Supply Networks, e.g.,
 - Demand Planning and Management (subset of Connected Customer)
 - Supplier Collaboration (subset of Intelligent Supply)



SECTION D: IDENTIFY INITIATIVES TO ADDRESS GAPS





Section D Overview

Section D Learning Objectives

- Develop a portfolio strategy and an initial portfolio of transformation initiatives.
- Use strategic assessment to determine scope, impact, and effort of initiatives.
- Use a process to sequence and prioritize initiatives.
- Categorize projects in a prioritization matrix.

Collect and Validate Data

Potential Sources

- Channel partner strategies, control towers, analytics
- Internal customer data
- Supplier contracts and SLAs
- Inventory data
- Transportation tracking data
- Social media analytics, weather data, etc.

Validation Checks

- Valid sample sizes at necessary level of precision and confidence
- Standardized master data
- Outliers: valid or invalid
- Missing data
- Duplicate data merged
- Up-to-date data
- Clear ownership of each data type



Strategic Assessment

- Do the supply chain priorities align with business unit or organizational strategy? Do they align with the operationalized customer segments identified?
- Does the to-be process architecture address the end-toend scope of this supply chain segment?
- Will processes be integrated, documented, and supported by valid and timely data? Will they be adaptable to new organizational learning or strategy shifts?



Validate Problem Weights and Produce First Draft of Portfolio

Review current defect rate.

Take small random sample of records or other data.

Perform root cause analysis.

Adjust problem weights based on results.




Turning Problems into Opportunities

- Defect identification and discussion can be contentious.
- Estimate actual profit potential for each proposed project.
 Benefits and known tradeoffs
- Costs may also require estimation.
 - Seek actual data for estimates to use as a proxy.
- Be sure to document all assumptions that are made.



Refine Quantitative/Qualitative Success Targets and Benefits Per Project

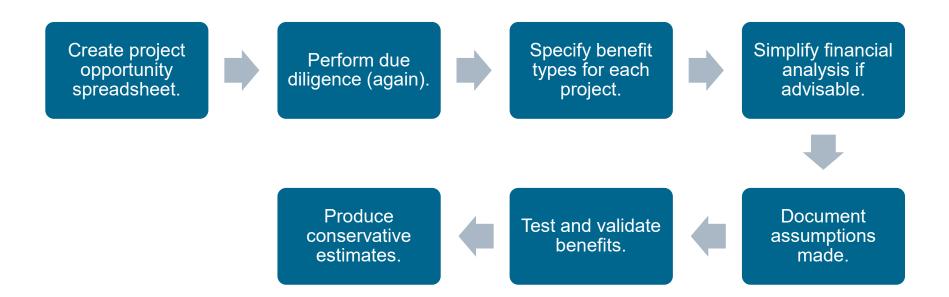



Steering Team Review and Go/No-Go Phase Gate

- Evangelist and selected design team members present project portfolio to steering team and executive sponsor.
- Working with external parties on a transformation:
 - Have clear and consistent messaging among all points of contact with these parties.
 - Agree on goals internally before presenting externally.
 - Reflect final decisions in internal team goals.



Apply Project Sequencing

Mandatory dependencies

 Inherent in nature of activities or regulatory or contractual requirement

Discretionary dependencies

- Based on best practices
- Increases risk to ignore



Plan Quick Wins, Tactical Initiatives, and Strategic Initiatives

High	Quick wins	Sponsor issue	
Impact, improvement, return	 Change in few processes 80/20: high impact Inexpensive change Easy to back out High ROI Quick deployment 	 Change in many processes 80/20: high impact Expensive change Difficult to back out High ROI Long deployment 	
prov	Nice to have	Consider carefully	
MoT Impact, im	 Change in few processes 80/20: low impact Inexpensive change Easy to back out Low ROI Quick deployment 	 Change in many processes 80/20: low impact Expensive change Difficult to back out Low ROI Long deployment 	
	Low Complexity, effort, risk Hi		

91



Apply Additional Priority Criteria

		Weight	Score (–3 to 3 for all but aversion factors; there use –3 to 0)	Total
Internal benefits	Revenue growth	10%	2	0.20
	Cost avoidance	10%	2	0.20
	Cost reduction	5%	1	0.05
	Cash-to-cash cycle time improvement	20%	3	0.60
Customer	Reliability	10%	2	0.20
benefits	Responsiveness	5%	0	0.00
	Agility	10%	1	0.10



Build Alliances and Trust

- Building alliances and trust with influential stakeholders and decision makers is vital.
 - A waste if decision makers do not act on the information
 - Strategy for marketing the benefits to stakeholders
 - Incorporate feedback
 - Incremental project benefits (well timed quick wins)
- For strategic initiatives that increase headcount or capital investment, consider offering up cuts elsewhere.



SECTION E: INITIATE TRANSFORMATION WORK STREAMS AND PROJECTS





Section E Overview

Section E Learning Objectives

- Create project charter.
- Lead program kickoff meeting.
- Create resource management plan.
- Negotiate for necessary resources.
- Implement stakeholder management plan, communication management plan, and change management plan.

Topic 1: Create Project Charters and Hold a Transformation Program Kickoff

Collect Business Requirements: Align with Needs

Corporate mission, vision, strategy, and goals

Customer preferences

Requirements from external partners

Employee preferences

Regulatory requirements





Project Schedule and Milestones

Project Schedule Development

- Starts with the project or portfolio scope and work breakdown structure
- Identifies major milestones
- Requires more than one pass

Non-Milestone Activities

- Regular meetings
- Working sessions
- Planned project alignment evaluations
- Planned communication
- Outreach efforts to stakeholders
- Other tasks (risk evaluation/ mitigation)
- Schedule management plan



Project Charter Elements


Purpose	Objectives	Business requirements	Assumptions and constraints
Project scope	Risk register	Milestones schedule	Budget
Stakeholder summary	Approval summary	Project manager	Project sponsors



Topic 1: Create Project Charters and Hold a Transformation Program Kickoff

Hold a Transformation Program Kickoff

- A kickoff meeting must take place.
- Include all the major participants involved in the project.

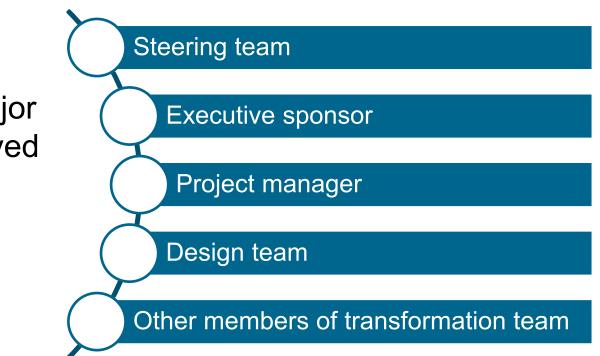



Topic 2: Develop Resource Management Plan

Resource Management Plan Components

Higher level: Overall plan

- Increased uncertainty
- Balance needs of program
- Capacity constraints depending on progress
- Interdependencies

Lower level: Major component plans

- Decreased uncertainty
- Consider only requests from component itself





Topic 2: Develop Resource Management Plan


Negotiate for Desired Resources

- Once the resource plan has been created, the identified resources must be acquired.
 - Resources from many organizational areas
 - Ensure fit and check for problematic employees being assigned
 - Contracting with external contractors
- For material resources
 - Getting the best deals and conserving financial resources may help provide later flexibility





Mapping Stakeholders and Their Needs

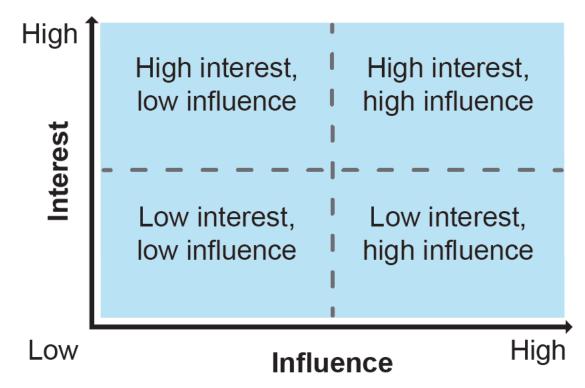



Managing Relationships

Team-building exercises

Mutual goal setting


Ongoing involvement of leadership and management

Communicating through opposition

One-on-one or small group meetings to work through opposition



Communication Process and Dimensions

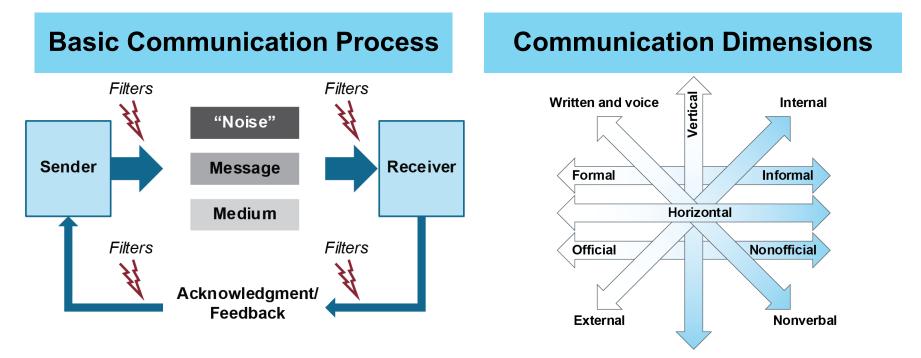

Source: Holmes Corporation. Used with permission.



Communication Plans

- Account for outgoing and incoming communication
- Tailored to needs
- Specified media and protocols
- Responsible individuals and roles

Document: Communications Management Approach Project: Project 1, CPFR, West Coast Pilot, Phase 1—Costking Cust	Author: Project Manager omer
1. Introduction:	
The CPFR project is a collaboration between Sample, Inc., and its key requires strong external communications. Costking is the collaboration	
2. Communication Procedure:	
 The project manager is responsible for all internal communication report weekly to the steering committee's project subcommittee u The director of sales is responsible for all formal external commu technical communications to relevant SME team members. 	ising a summary report.
3. Tools and Techniques:	
 The project manager will use the project portal for all internal condocuments. The director of sales will use site visits, virtual meetings, and a neparticipating customers. 	
4. Records:	
The following reports will be issued for internal communications: summ project results report, issue report, lessons learned report, change man newsletter (electronic).	
5. Timing of Communication Activities:	
The project manager will meet with the project subcommittee on a biv presentation for go/no-go at each milestone.	veekly basis and have a formal



Data Visibility and Transparency of Project Outcomes


Different stakeholders will require different information at different cadences and for different purposes.

Broad data visibility is inappropriate.

It is important to be consistent and intentional with communications.



Building Communication Channels



Topic 4: Document Change Management Plan(s)

Assess Change Management Requirements

First-order change

- Change to process
 or procedures
- Adjustment to systems
- Reversable
- Nontransformable

Second-order change

- Change in strategic direction
- Requires individuals to learn new skills
- Irreversible
- Transformable


Third-order change

- Change in values, culture, founding principles
- Very difficult; individuals may leave
- Iterative
- Irreversible
- Transformational



Topic 4: Document Change Management Plan(s)

Gaining Buy-In: Key Causes of Resistance






Topic 4: Document Change Management Plan(s)

Design Training

- Most effective to train when systems and processes go live.
- Training needs assessment
 - Performance requirements
 - Associated knowledge, skills, and abilities







SECTION F: DEVELOP AND ITERATE PRELIMINARY TRANSFORMATION BUSINESS CASES





Section F Overview

Section F Learning Objectives

- Identify targeted value drivers.
- Quantify anticipated value of improvements.
- Calculate ROI.
- Determine necessary resources.
- Identify KPIs.
- Create business case messaging.
- Present business case to leadership.



Use a Business Case Development Process

Benefits

- Foster strategic thinking.
- Improve decision-making efficiency and quality.
- Enable comparison of alternatives.
- Establish criteria.

Questions to Answer

- Is the project achieving the anticipated benefits?
- Are the assumptions observed to be accurate in reality?
- Is the business case justification still valid?



Set Targeted Value Drivers

- Business case: opportunity to create quantifiable benefits for an organization such as new revenue or cost or lead time reduction
- Benefits may be realized at different points of a project.
- Consider qualitative benefits:

Creating more flexible systems to adapt to future conditions Increasing visibility and understanding among supply chain partners Improving working conditions (and thus morale) of employees



Topic 2: Quantify Financial Value of Supply Chain Improvements

Economic Levers and Measures

Major Economic Levers

- Revenue
- Costs
- Net fixed assets (fixed capital)
- Working capital
- Capital expenditure (capex)

Important Measures

- Net working capital
- Current ratio
- Time value of money
- Discounted cash flow
- Break-even point
- Contribution margin



Topic 2: Quantify Financial Value of Supply Chain Improvements

Related Analyses

Cost-Volume-Profit Analysis

• "Study of how profits change with various levels of output and selling price" (*Dictionary*)

Break-Even Analysis

• "Study of the number of units or amount of time required to recoup an investment" (*Dictionary*)

Estimate ROI

ROI is calculated using the following formula:

Return on Investment = Gain from Investment – Cost of Investment Cost of Investment

Residual income is calculated in the following manner.

Residual Income =

Operating Income – (Minimum Required Rate of Return x Operating Assets)



Topic 2: Quantify Financial Value of Supply Chain Improvements

Estimate ROI, continued

- Payback period is "the period of time required for the stream of cash flows resulting from a project to equal the project's initial investment." (*Dictionary*)
- Payback period:

Payback Period = $\frac{\text{Cost of Investment}}{\text{Annual Cash Savings}}$



Determining Necessary Resources

Focus Areas

- Current/core supply chain functions
- New strategies
- Entirely new functions or operations

Funding Models

- Self-funding
- Funding from outside the managing unit
- External funding and management
- Collaborative funding



Topic 3: Determine Resources Needed and Estimate Cost and Schedule

Tools

Analysis of alternatives	 Cost, inputs, outputs, time frame E.g., make, rent, or buy 	
Bottom-up estimating	 Individual estimates rolled up 	

Software tools

Project management software




Determine How Project Spend Will Be Managed

The financial management plan records the following information:

- Schedules and milestones
- Initial budget
- Reporting mechanisms
- Financial metrics used to monitor program
- Associated operational and infrastructure costs
- Component payment schedules

Topic 3: Determine Resources Needed and Estimate Cost and Schedule

Estimate Cost and Schedule

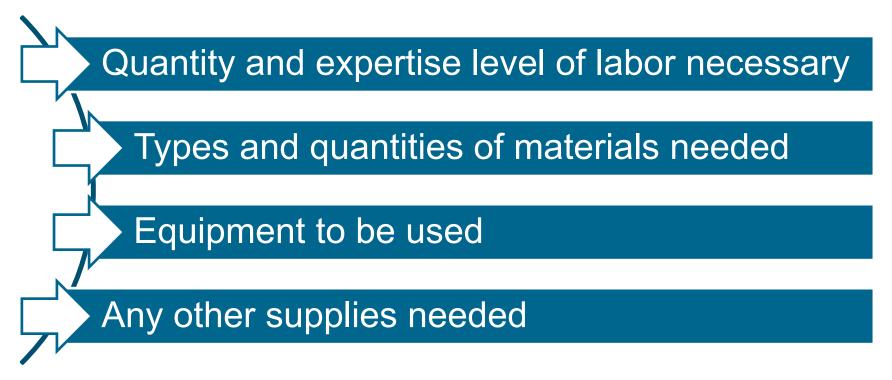



Topic 4: Select Transformation Program KPIs

Define Metrics and Measurement Processes

Overall progress against schedule

Project performance against budget

Individual process/project progress against schedules

Number of change requests

Number of approved/rejected requests

Project benefits realization

Team member performance



Topic 5: Craft Messaging Content

Communicate the Need and Future State of Success

- Marketing stakeholders can help make business case persuasive.
- Identify and understand target audience

Examples of questions for decision makers:

- What do they value?
- Are they risk-averse or aggressive?
- What is the climate of the organization and marketplace, and how does this affect the positioning of the business case?
- Are there supportive stakeholders who have a strong relationship with the decision makers and can help present the case or otherwise help influence them?
- Do decision makers have areas of interest within the organization that they consistently focus on?
- Does someone in the decision-making group stand to lose something or have other reasons to oppose the project?



Topic 5: Craft Messaging Content

Present the Business Case, Follow Up, and Take Next Steps

Once you have prepared your presentation:

- Schedule a meeting for the presentation.
- Maintain professionalism.
- Formally present the business case.
- Allow time for questions and discussion.
- Follow up no matter whether the project was approved/denied.





SECTION G: POST-APPROVAL TASKS






Section G Overview

Section G Learning Objectives

- Assemble and complete the project portfolio.
- Use various tools to expand on the brainstorming processes.
- Work around identified resource constraints.
- Refine the business case based on new information.
- Create a portfolio management plan.

Project Portfolio Scope

- Project portfolio scope statement
- Analysis of selected metrics and identification of any gaps
- Work breakdown structure, which includes other project documentation






Tools to Expand on Brainstorming/Planning Processes

- Brainstorming repeated for approved project goals and tasks
- Tools to help expand on brainstorming and planning:
 - Nominal group technique: each person shares an idea, and the group discusses and prioritizes them
 - Mind mapping
 - Rich pictures
 - Affinity diagrams
 - Cause-and-effect diagrams
 - 5W2H framework

Mind Mapping

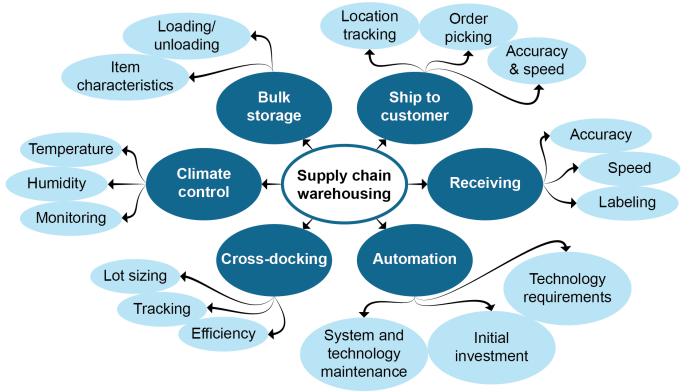



Rich Pictures

Use when structures and processes are unclear/ undefined.

Avoid using too much commentary. Don't rely on preconceived systems and organizations. Include social roles and expected behaviors from individuals.

Include yourself in the picture to highlight your roles in the system.




Affinity Diagram

Issue: Product recall causes					
Inspection	Customer feedback	Product materials			
Frequency	Costs	Return processes			



Cause-and-Effect Diagrams

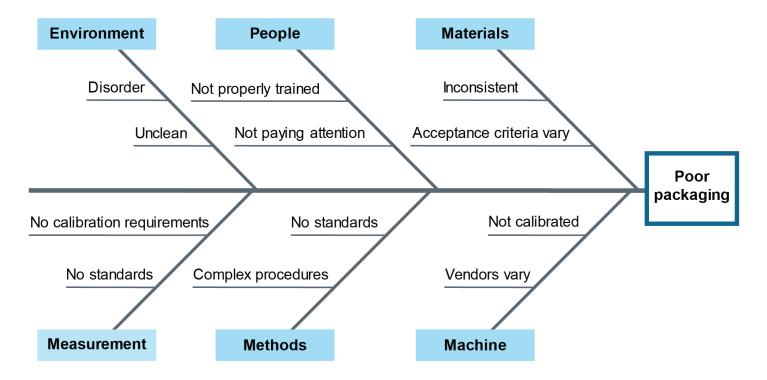



5W2H Framework Who? How What? much? **5W2H** When? How? Why? Where?

Validate Financial and Customer Service Commitments

Validate Commitments

- Following approval, revalidate
 - Previously identified costs
 - Initial commitments.
- Justify requests for additional resources.

Working Around Constraints

- There will be planned tasks that exceed the available resources.
 - Finance availability may be an issue.
 - Negotiate to get additional resources.



Evaluate and Select People and Solutions

Selection of the project team is crucial.

- Use a detailed organizational chart
- Capture team members' skills, duties, and other key details.

Employee	Current position	Job profile	Seniority level	Skills gap between current level and next level



Auditing

- Set up auditing and assessment tools during project initiation.
- Define
 - Audit scope
 - Audit criteria
 - Specific assigned roles and responsibilities.
- Use an audit team that is separate from the project team when possible.

Select Consulting Partners and SC Business Outsourcing Partners



- Addresses labor availability constraints.
- Potential addition of missing bestpractice expertise.
- Expertise leads to increased efficiency.
- Energy injection into project.
- Outside perspectives may generate additional insight.
- May have ability to sway decision makers.



- More expensive.
- May be difficult to find qualified consultants.
- Consultants require training and time to learn details of the business.
- Presence of external consultants may drive perceptions that harm implementation.
- Increased risk of scope creep.



Topic 3: Refine Supply Chain Transformation Business Case

Refining the Business Case

- Update business case as initial work begins on project.
- Supply updated and increasingly detailed information.
 Helps shore up promised financial, capital, and labor support
- Reassess financial value of supply chain improvements.
- Do ongoing analysis of alternatives.
 - Selecting suppliers, consultants, software
 - May be contractual obligation



Topic 4: Establish and Align Portfolio Governance and Draft Execution Plans

Portfolio Management Plans and Definition

Governance	Oversight	Change management
Balance and dependency management	Prioritization	Communication, risk, procurement, compliance



Ensure Proper Funding, Support, and Oversight Over Project Management and Risk Management

- Set processes to ensure project is monitored
 - Weekly basis
 - Funding, resources, task barriers, struggling persons/teams
- Tracking
 - Color-coded systems
 - Easy-to-monitor indicators

What work was done last week?

What work has been completed against the plan?

What work is planned for the coming week?

What issues are impeding progress?



Topic 4: Establish and Align Portfolio Governance and Draft Execution Plans

Set Key Steps, Milestones, and Time Line

